

2020년 가로수 집중관리 거리경관 개선(시 참여)

< 은행나무 암·수교체, 신규식재, 메워심기 등 >

2020. 3.

동 작 구 청



■ 사업소개


사업명	2020년 가로수 집중관리로 거리경관 개선(시 참여)
사업내용	<ul style="list-style-type: none"> - 대상지 : 현충로 - 사업기간 : '20. 1. ~ 6. - 사업비 : 50백만원 - 사업내용 : 은행나무 암수교체, 신규식재, 메워심기 등

■ 위치도



■ 가로수 노선현황

노선현황	<ul style="list-style-type: none"> - 노선명 : 현충로 - 노선폭 : 35~40m - 연장 : 3km - 수량 : 은행나무 373주(수나무 237, 암나무 136)
------	---

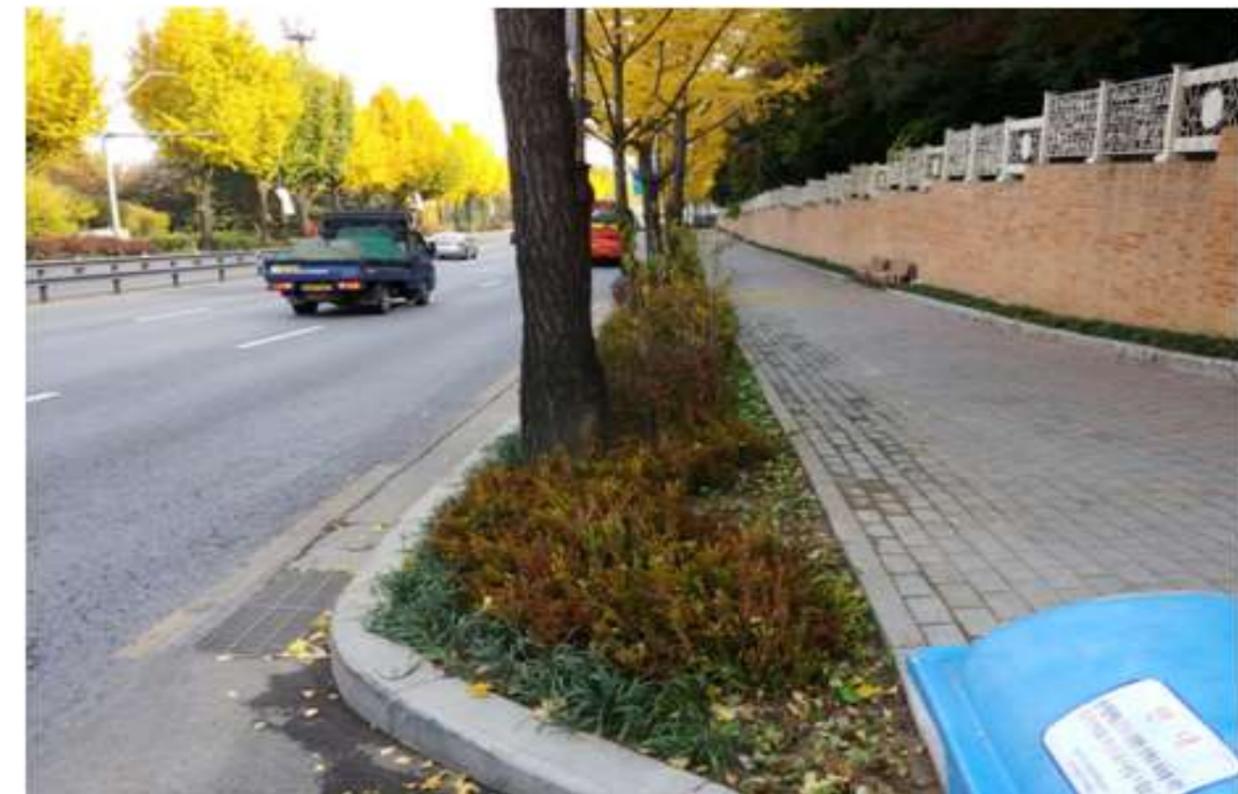



■ 최근 2년간 현충로 가로수 변동사항

'19년	<ul style="list-style-type: none"> - 사업명 : '19년 은행나무(가로수) 암나무 바꿔심기 - 기간 : '19. 11. ~ 12. - 규격 : H5.0*B15 - 내용 : 수형수세 등이 불량한 은행나무 암나무를 수나무로 바꿔심기 - 수량 : 5주 / 상도로 4주 - 예산액 : 11백만원(시비)
'20년	<ul style="list-style-type: none"> - 사업명 : '20년 가로수 집중관리로 거리경관 개선 - 기간 : '20. 1. ~ 6. - 규격 : H4.0*B12 - 내용 : 은행나무 암수교체, 신규식재, 메워심기 등 - 수량 : 48주(메워심기 35주, 신규식재 13주) - 예산액 : 50백만원(시 참여)

구분	은행나무	
수목사진		
원산지	중국동부	
양태적특성	잎/단풍	부채꼴 /황색
	꽃	4-5월 황록색
	열매	10월, 황색 구형
	수피	
생태적특성	수형	원추형
	근계	심근성
	내한성	강
	내공해성	강
	이식	용이
	성장속도	느림
유지관리	전정	매년 혹은 격년 동기 가지치기
가로수 특성	환경정화 수종 가을의 노란색 단풍이 아름다움 줄기가 직선으로 뻗어 건물의 딱딱한 선을 강조할 우려 있음	
적정 규격	B20	
성목 높이	30m	

■ '19년 바꿔심기 현황사진





'19년 바뀌심기 현황사진






■ 가로수 신규 식재지 주요 현황



- 기존 가로수
- 가로수 메워심기
- 가로수 신규식재

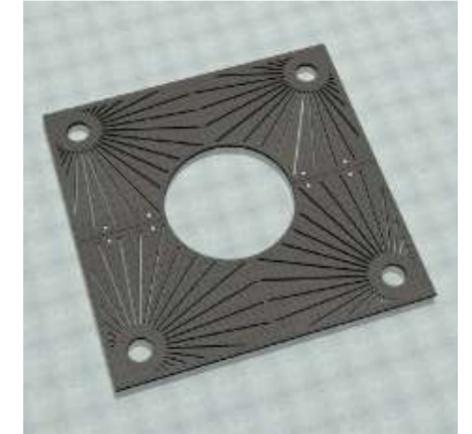

압연강재보호판



① 현황사진



② 지역 현황사진




③ 지역 현황사진



■ 가로수 신규 식재지 주요 현황



- 기존 가로수
- 가로수 메워심기
- 가로수 신규식재

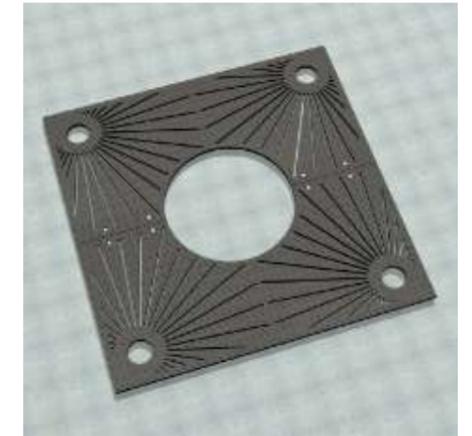

압연강재보호판



① 현황사진




② 지역 현황사진



③ 지역 현황사진



■ 가로수 신규 식재지 주요 현황

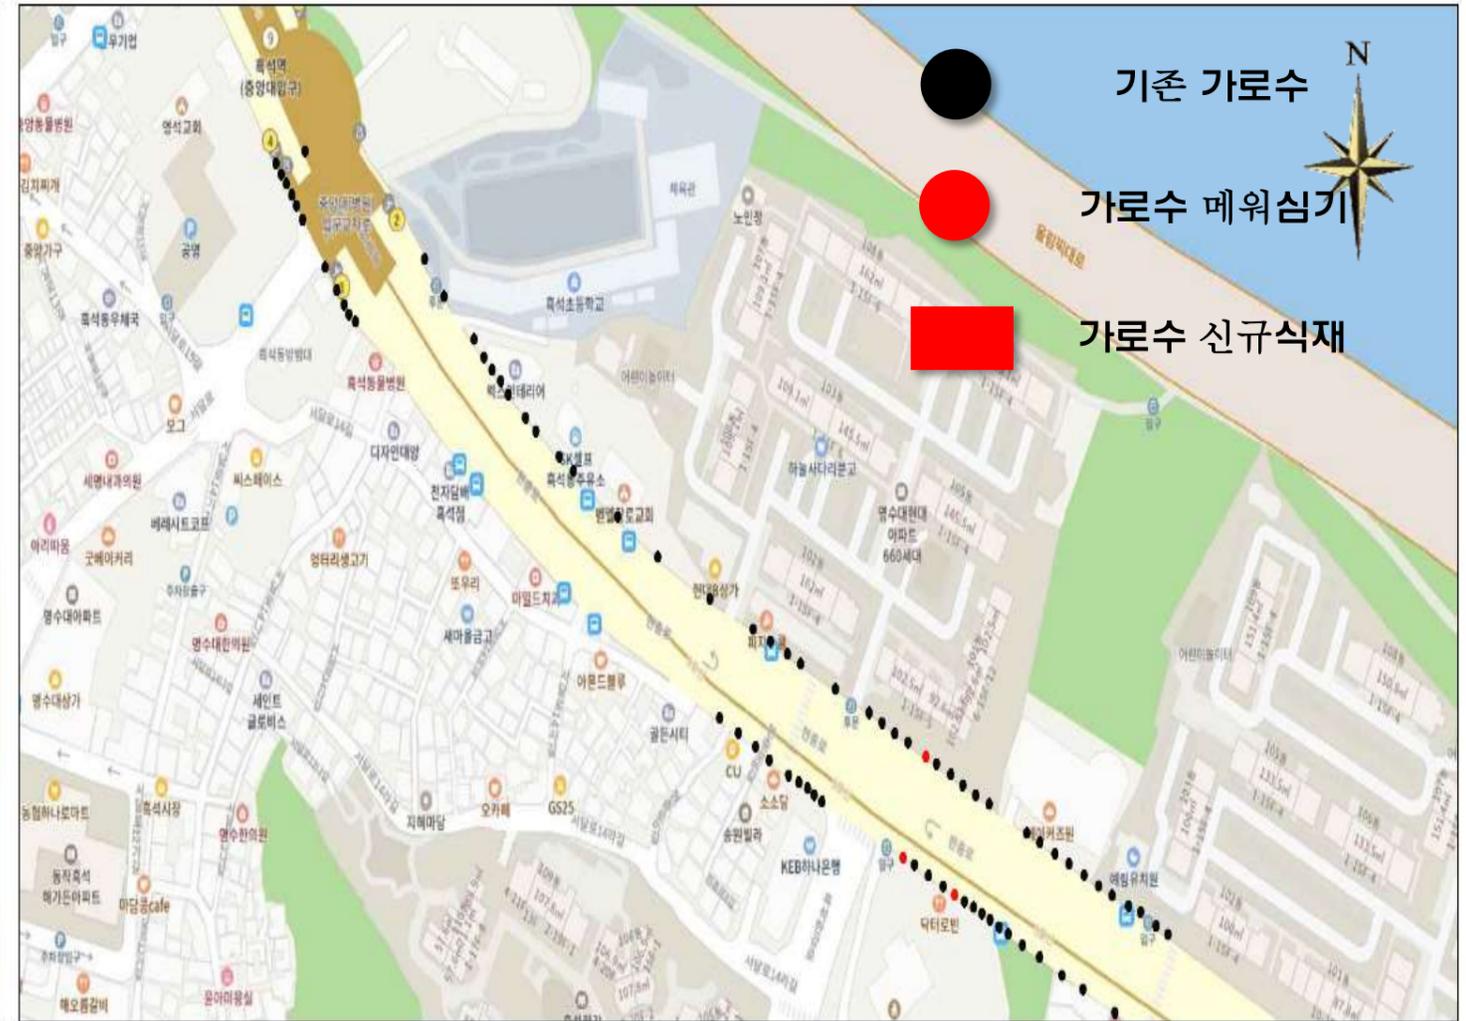

① 현황사진



② 지역 현황사진



③ 지역 현황사진






■ 가로수 신규 식재지 주요 현황



- 기존 가로수
- 가로수 메워심기
- 가로수 신규식재

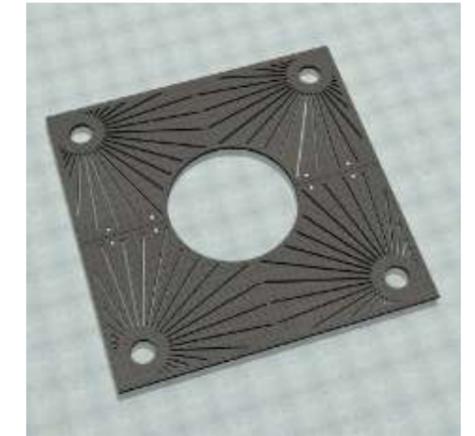


압연강재보호판






■ 가로수 신규 식재지 주요 현황

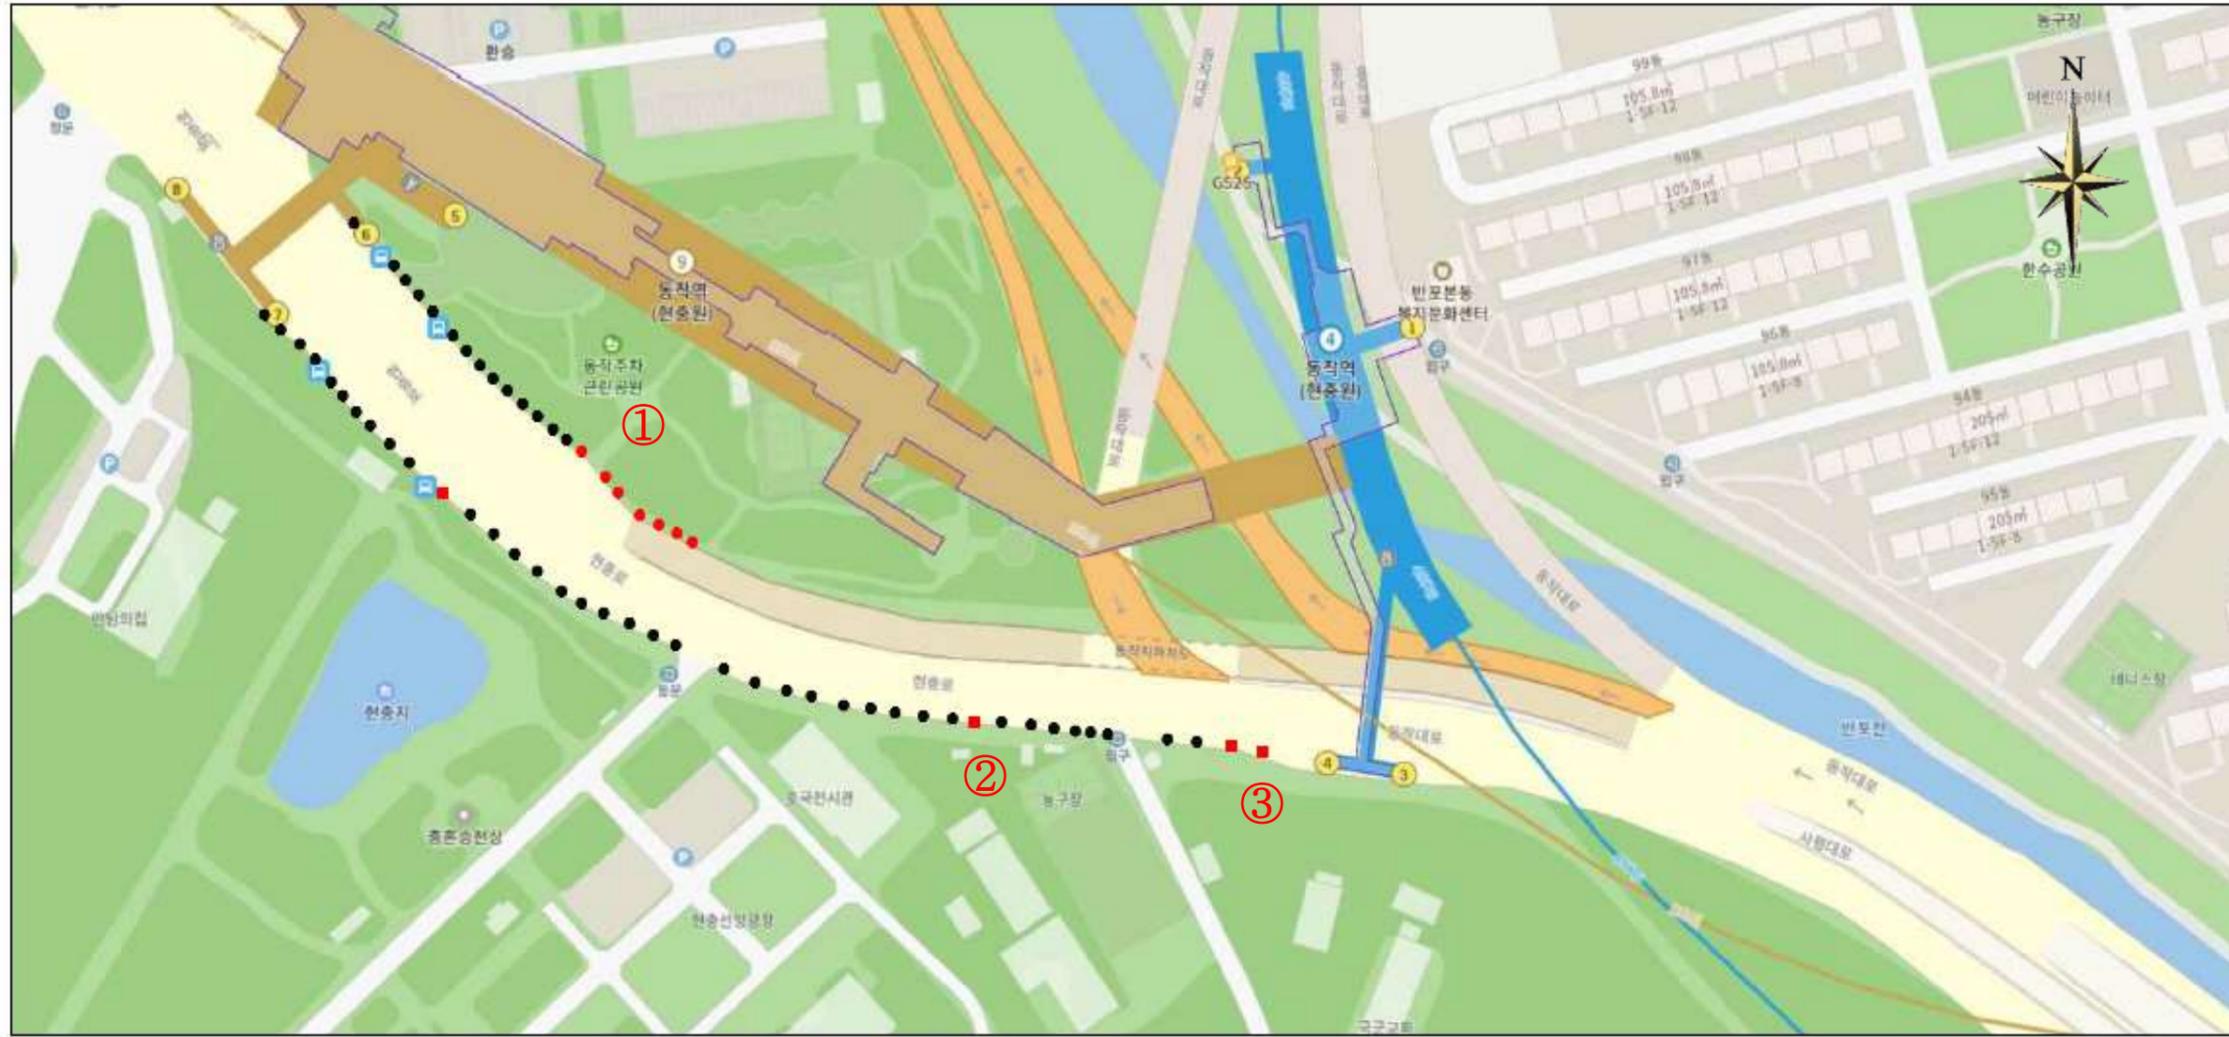

- 기존 가로수
- 가로수 메워심기
- 가로수 신규식재

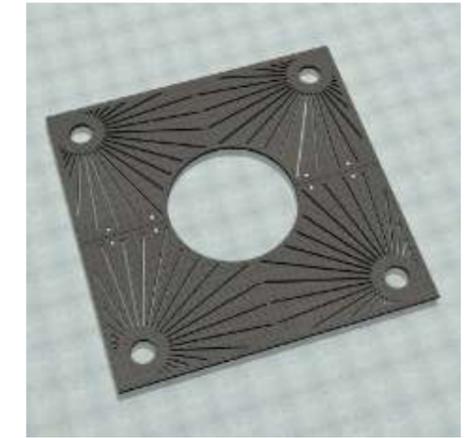

압연강재보호판



4. 개략공사비

2020년 가로수 집중관리로 거리경관 개선(시 참여)



구분	공종	수량	단위	단가	합계	비고
1. 식재공사	은행나무 식재	48	H4.5*B12	560,000	26,880,000	
2. 시설물공사	보호판, 보호틀 설치	13	조	465,000	6,045,000	
소계					32,925,000	
제경비		40	%		13,170,000	
공급가액					46,095,000	
부가가치세		10	%		4,609,500	
도급공사비					50,000,000	50,704,500
